Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PCC II-3	PCC II West Expansion (Finished Schedlue) 2 - Updating				
PCC II-3.1	NTP				
A1000	Receive NTP	0.0	01-Jun-22 07:00 AM		
A1020	Long Lead Submittals & Procuremer	30.0	01-Jun-22 07:00 AM	07-Jul-22 06:00 PM A	
A1010	Pre-Construction Meeting(s)	1.0	01-Jun-22 08:00 AM	02-Jun-22 08:00 AM	
A1030	Standard Submittals & Procurement	48.0	08-Jul-22 07:00 AM A	03-Sep-22 02:00 PM	
PCC II-3.2	MOBILIZE & SITE SET-UP				
A1050	Mobilize to Site	2.0	02-Jun-22 08:00 AM	04-Jun-22 09:00 AM	
A1060	Install Temp Fencing	4.0	04-Jun-22 09:00 AM	09-Jun-22 10:00 AM	
A1070	Install Temp Offices & Trailers	4.0	04-Jun-22 09:00 AM	09-Jun-22 10:00 AM	
A1080	Install Temp Utilities	4.0	04-Jun-22 09:00 AM	09-Jun-22 10:00 AM	
A1120	Mobilize Equipment	2.0	04-Jun-22 09:00 AM	07-Jun-22 10:00 AM	
A1130	Set-up Pedestrian Access	2.0	04-Jun-22 09:00 AM	07-Jun-22 10:00 AM	
PCC II-3.10	PHASE 1				
PCC II-3.10.1	PHASE 1 PRE-DEMO				
A1090	Install Phase 1 Construction Barrier	7.0	09-Jun-22 10:00 AM	17-Jun-22 12:00 PM	
A1100	Isolate Phase 1 Utilities	2.0	09-Jun-22 10:00 AM	11-Jun-22 11:00 AM A	
A1110	Set-up Neg Air and Air Scrubbers	1.0	17-Jun-22 01:00 PM	18-Jun-22 01:00 PM	
PCC II-3.10.4	PHASE 1 DEMO				
A1140	Establish a construction opening	1.0	09-Jun-22 10:00 AM	10-Jun-22 10:00 AM	
A1150	Install Secure Temp Door	1.0	10-Jun-22 10:00 AM	11-Jun-22 11:00 AM A	
A1160	Demo Interior Finishes	15.0	18-Jun-22 01:00 PM	08-Jul-22 08:00 AM A	
A1170	Install & Maintain Fire Protection	15.0	18-Jun-22 01:00 PM	08-Jul-22 08:00 AM A	
A1180	Demo Slab Trenches Phase 1	5.0	08-Jul-22 08:00 AM A	22-Jul-22 10:00 AM A	
A1190	Demo Roof @ Stair 1	2.8	16-Sep-22 07:00 AM*	19-Sep-22 06:00 PM	54.5
PCC II-3.10.8	PHASE 1 BUILDOUT				
A1200	Frame Interior Walls	20.0	24-Jun-22 07:00 AM	01-Sep-22 04:00 PM	
A1240	RI new Fire Protection	10.0	24-Jun-22 07:00 AM	18-Aug-22 11:00 AM	
A1220	RI Below Grade Plumbing	4.0	14-Jul-22 10:00 AM A	19-Jul-22 12:00 PM A	
A1230	RI MEP	16.0	19-Jul-22 04:00 PM A	31-Aug-22 11:00 AM	
A2770	Pour Back Trenches Phase 1	2.0	09-Aug-22 07:00 AM	12-Sep-22 06:00 PM	
A1260	Frame Soffits and Hard Lids	17.2	19-Aug-22 07:00 AM	22-Sep-22 06:00 PM	274.6
A1270	Insulate and install GWB	20.0	31-Aug-22 07:00 AM	24-Sep-22 02:00 PM	36.5
A1390	Install Structural Upgrades Stair 1	6.0	13-Sep-22 07:00 AM	13-Sep-22 06:00 PM	
A1280	Tape GWB	20.0	13-Sep-22 11:00 AM	06-Oct-22 06:00 PM	33.9
A1210	Frame New Exterior Penthouse	6.0	20-Sep-22 07:00 AM	27-Sep-22 09:00 AM	271.6
A1380	Install Metal Stairs @ Stair 1	4.0	20-Sep-22 07:00 AM	23-Sep-22 06:00 PM	54.5
A1400	Install Roofing at Stari 1 Penthouse	4.0	24-Sep-22 08:00 AM	29-Sep-22 09:00 AM	102.6
A3100	Install Coiling door Tubes and Colum	2.0	26-Sep-22 07:00 AM*	27-Sep-22 06:00 PM	99.8
A1370	Install Coiling Grilles	4.0	28-Sep-22 07:00 AM	03-Oct-22 09:00 AM	99.8
A1290	Paint GWB	15.0	30-Sep-22 04:00 PM	19-Oct-22 11:00 AM	33.9
A2990	Pour Stair 1 Treads	4.0	19-Oct-22 07:00 AM	24-Oct-22 09:00 AM	82.4
A1350	Install Door Frames	4.0	19-Oct-22 11:00 AM	24-Oct-22 02:00 PM	33.9
A1430	Install Wall Protection	6.0	19-Oct-22 11:00 AM	26-Oct-22 02:00 PM	39.9
A2890	Install HD-1 Shelving System Compl	5.0	19-Oct-22 11:00 AM	25-Oct-22 02:00 PM	81.0
A1300	Install Ceiling Grid	12.0	24-Oct-22 02:00 PM	07-Nov-22 06:00 PM	33.9

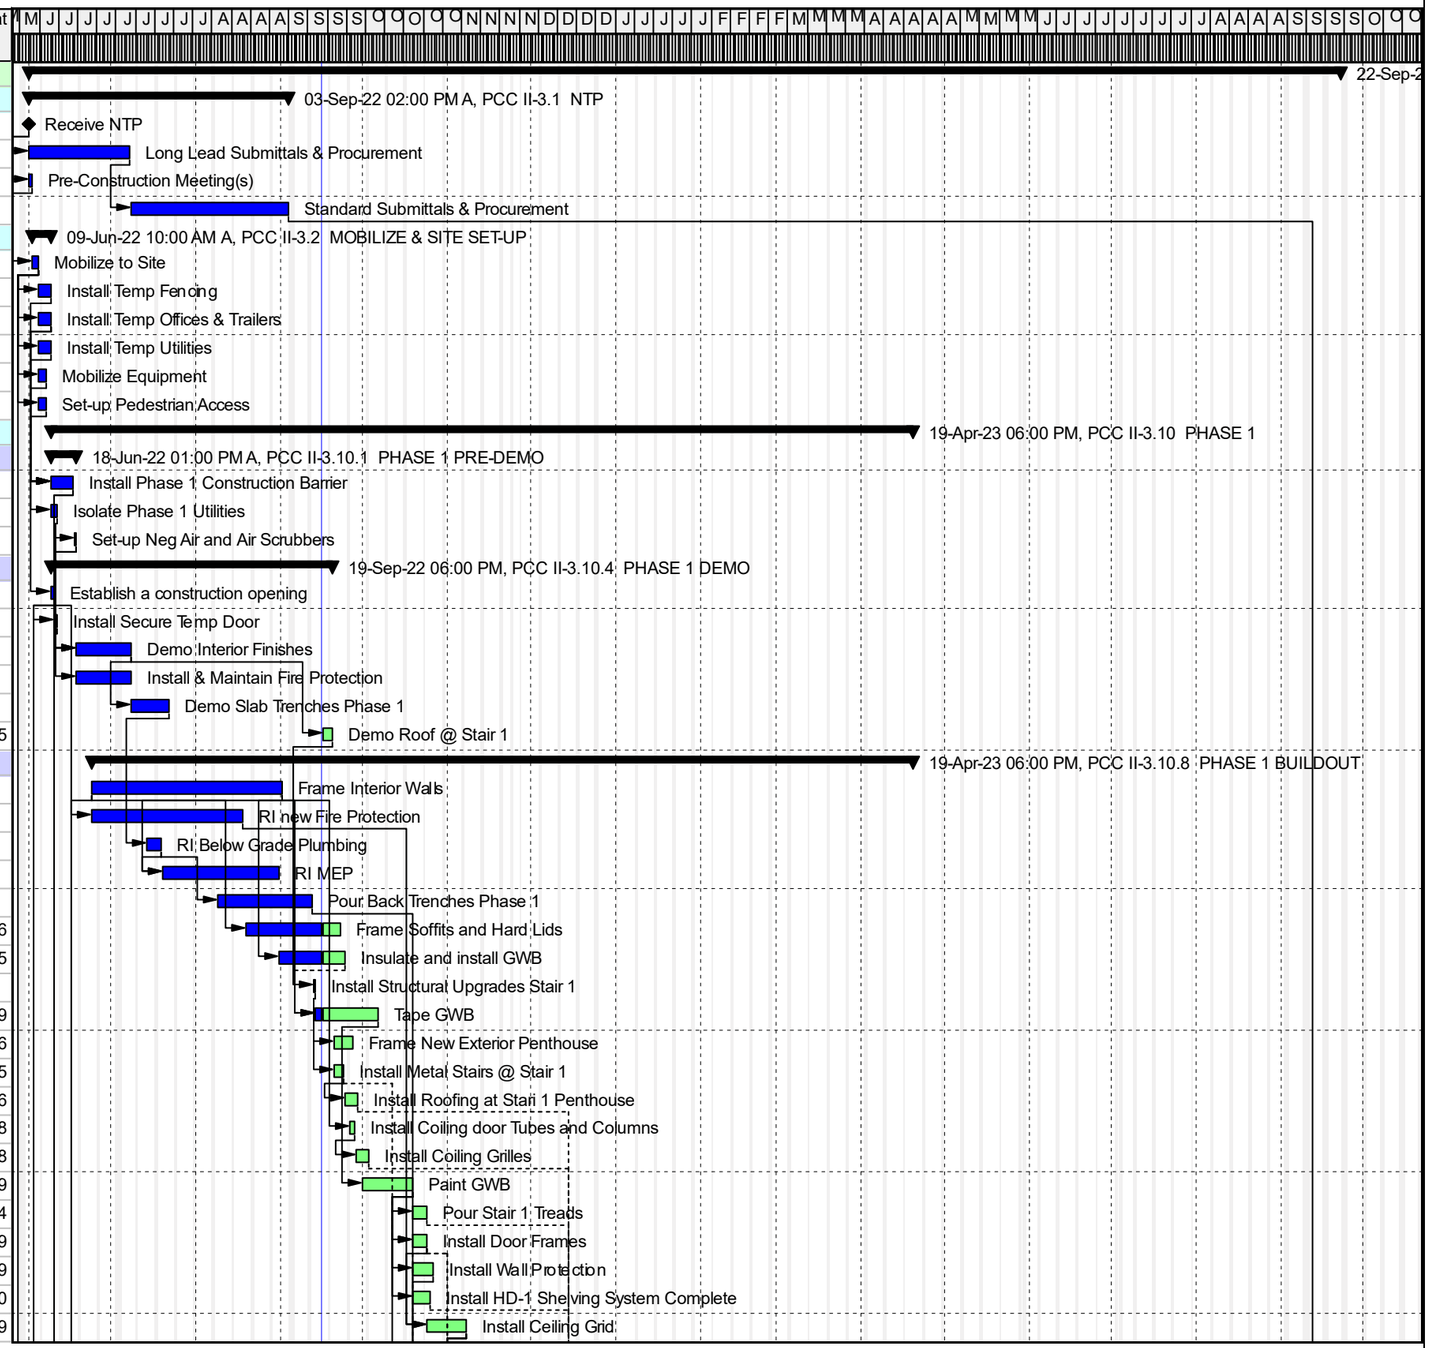

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
A1330	Prep Floors	4.0	26-Oct-22 02:00 PM	31-Oct-22 04:00 PM	39.9
A1440	Install Casework and Trim	12.0	31-Oct-22 04:00 PM	15-Nov-22 09:00 AM	40.7
A1310	Install Electrical Fixtures	12.0	08-Nov-22 07:00 AM	22-Nov-22 11:00 AM	52.0
A1320	Install Sprinkler and HVAC Trims	8.0	08-Nov-22 08:00 AM	17-Nov-22 04:00 PM	49.0
A1340	Install Flooring	12.0	08-Nov-22 08:00 AM	23-Nov-22 04:00 PM	30.0
A2780	Install Ceiling Tiles	6.0	22-Nov-22 11:00 AM	30-Nov-22 02:00 PM	52.0
A1360	Install Doors & Hardware	6.0	23-Nov-22 04:00 PM	01-Dec-22 06:00 PM	46.6
A1460	Install Demountable Partitions	6.0	23-Nov-22 04:00 PM	01-Dec-22 06:00 PM	44.6
A1450	MEP Trim	12.0	24-Nov-22 08:00 AM	09-Dec-22 04:00 PM	30.0
A1670	Install Conveyors and Pharmacy Equ	5.0	24-Nov-22 08:00 AM	30-Nov-22 04:00 PM	45.1
A1420	Install Accessories	4.0	09-Dec-22 04:00 PM	14-Dec-22 06:00 PM	34.0
A1470	Install Furniture	6.0	15-Dec-22 07:00 AM	22-Dec-22 09:00 AM	34.0
A1480	Install Appliances	4.0	15-Dec-22 07:00 AM	20-Dec-22 09:00 AM	36.0
A1490	Contractors Punchlist	10.0	22-Dec-22 09:00 AM	04-Jan-23 11:00 AM	34.0
A1410	Install Siding at Stair 1 Penthouse	6.0	12-Apr-23 04:00 PM	19-Apr-23 06:00 PM	103.4
PCC II-3.10.7 PHASE 1 SUBSTANTIAL COMPLETION					
A1530	TAB Phase 1	4.0	09-Dec-22 04:00 PM	14-Dec-22 06:00 PM	50.0
A1540	Commissioning Phase 1	4.0	15-Dec-22 07:00 AM	20-Dec-22 09:00 AM	50.0
A1500	Final Cleaning	4.0	04-Jan-23 11:00 AM	09-Jan-23 02:00 PM	175.0
A2860	Substantial Completion Phase 1	4.0	04-Jan-23 11:00 AM	09-Jan-23 02:00 PM	34.0
A1510	Owner's Punchlist	2.0	09-Jan-23 02:00 PM	11-Jan-23 02:00 PM	175.0
A1680	Obtain CCO for Phase 1	0.0		09-Jan-23 02:00 PM	34.0
A1520	Punchlist Corrections	10.0	11-Jan-23 02:00 PM	23-Jan-23 06:00 PM	175.0
A2760	Start Warranty for Phase 1	0.0	24-Jan-23 07:00 AM		175.0
A2900	Owner Takes Possession of New Spa	0.0	24-Jan-23 07:00 AM		175.0
PCC II-3.9 PHASE 2					
PCC II-3.9.4 PHASE 2 PRE-DEMO					
A1590	Install Phase 2 Construction Barriers	4.0	17-Jun-22 01:00 PM A	22-Jun-22 03:00 PM A	
A1600	Isolate Phase 2 Utilities	4.0	22-Jun-22 03:00 PM A	27-Jun-22 05:00 PM A	
A1610	Install Neg. Air and Scrubbers	4.0	22-Jun-22 03:00 PM A	27-Jun-22 05:00 PM A	
PCC II-3.9.1 PHASE 2 DEMO					
A2870	Remove Trees and Shrubs	4.0	04-Jun-22 09:00 AM A	09-Jun-22 10:00 AM A	
A1560	Demo SIte Improvements for new Ac	2.0	10-Jun-22 10:00 AM A	13-Jun-22 12:00 PM A	
A1570	Grub the Addition Footprint	2.0	13-Jun-22 01:00 PM A	15-Jun-22 12:00 PM A	
A1550	Demo Brick Veneer	4.0	24-Jun-22 07:00 AM A	29-Jun-22 09:00 AM A	
A2790	Demo Interior spaces	10.0	27-Jun-22 05:00 PM A	11-Jul-22 10:00 AM A	
A1620	Demo Windows to get replaced	2.0	30-Jun-22 11:00 AM A	02-Jul-22 12:00 PM A	
A1580	Demo South Side Facade - Complet	6.0	22-Oct-22 08:00 AM	29-Oct-22 10:00 AM	35.4
PCC II-3.9.2 PHASE 2 BUILDOUT					
A1630	Excavate Footprint for New Addition	4.0	29-Jun-22 09:00 AM A	05-Jul-22 11:00 AM A	
A1640	Prep Subgrade for Footings	2.0	05-Jul-22 11:00 AM A	07-Jul-22 11:00 AM A	
A1690	Excavate for Utilities	2.0	07-Jul-22 11:00 AM A	09-Jul-22 12:00 PM A	
A1720	Form Footings	5.0	07-Jul-22 11:00 AM A	13-Jul-22 02:00 PM A	
A1700	Install UG Utilities	6.0	09-Jul-22 12:00 PM A	16-Jul-22 02:00 PM A	
A1730	Install Footing Reinforcement	2.0	13-Jul-22 02:00 PM A	15-Jul-22 02:00 PM A	
A1780	Install Embeds in Footings	2.0	15-Jul-22 02:00 PM A	18-Jul-22 04:00 PM A	

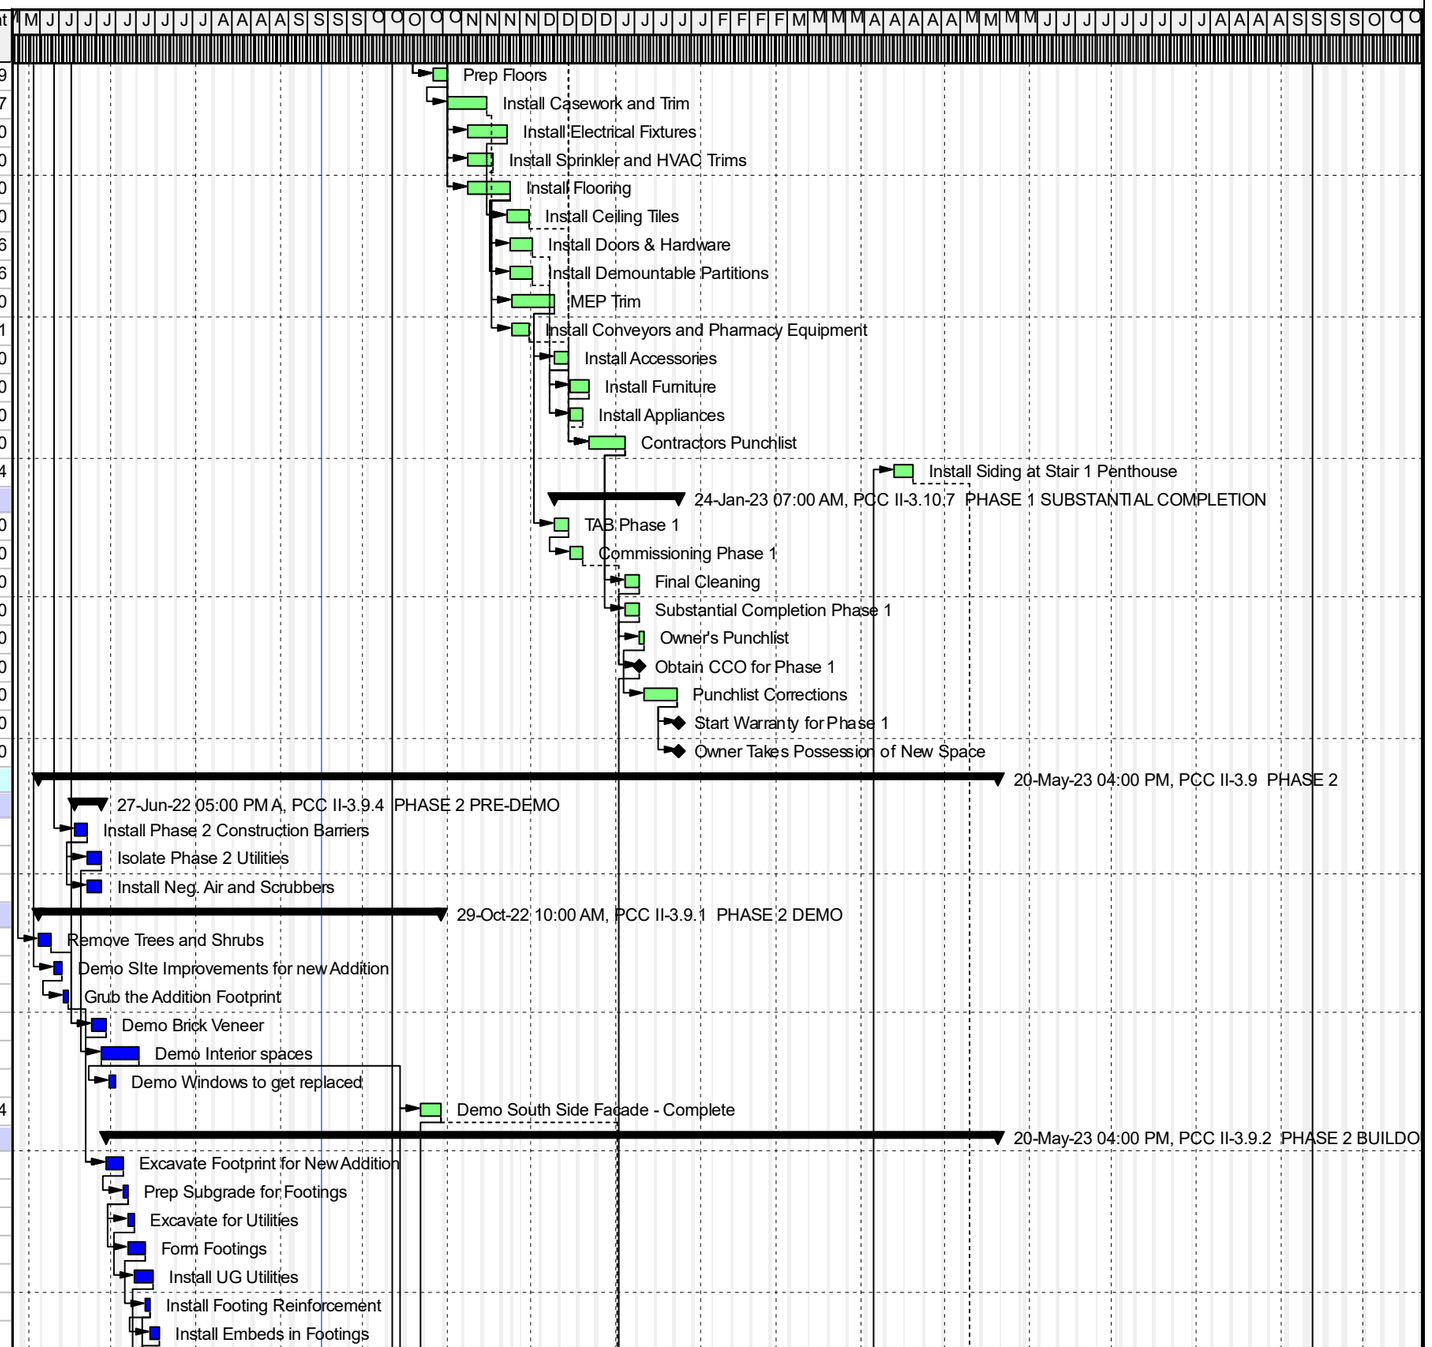

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
A1710	Backfill Utilities	2.0	16-Jul-22 02:00 PM A	19-Jul-22 04:00 PM A	
A1740	Place & Finish Footings	1.0	19-Jul-22 04:00 PM A	20-Jul-22 04:00 PM A	
A1810	Strip Footings	1.0	20-Jul-22 04:00 PM A	21-Jul-22 04:00 PM A	
A1750	Form Walls & Pilasters	6.0	25-Jul-22 07:00 AM A	01-Aug-22 09:00 AM	
A1760	Install Wall & Pilaster Reinforcement	4.0	01-Aug-22 09:00 AM	05-Aug-22 09:00 AM	
A1770	Install Anchorbolts	1.0	05-Aug-22 09:00 AM	06-Aug-22 10:00 AM	
A1790	Install Embeds in Walls	1.0	05-Aug-22 09:00 AM	06-Aug-22 10:00 AM	
A1800	Place and Walls & Pilasters	2.0	06-Aug-22 10:00 AM	09-Aug-22 11:00 AM	
A1820	Strip Walls & Pilasters	1.0	09-Aug-22 11:00 AM	10-Aug-22 11:00 AM	
A1830	Install Foundation Damproofing	2.0	09-Aug-22 11:00 AM	11-Aug-22 11:00 AM	
A1840	Install Foundation Insulation	1.0	09-Aug-22 11:00 AM	10-Aug-22 11:00 AM	
A1850	Install Pre-Cast Concrete Panels	7.0	15-Aug-22 11:00 AM	23-Aug-22 02:00 PM	
A1860	Backfill Footings & Walls	3.0	22-Aug-22 02:00 PM	25-Aug-22 02:00 PM	
A1880	Backfill Interior of addition for SOG	3.0	25-Aug-22 02:00 PM	29-Aug-22 04:00 PM	
A1870	Install Dimond Blockouts	2.0	29-Aug-22 04:00 PM	31-Aug-22 04:00 PM	
A1890	FineGrade Interior SOG	2.0	31-Aug-22 04:00 PM	02-Sep-22 04:00 PM	
A1900	Install UG MEP Rough In	6.0	01-Sep-22 08:00 AM	08-Sep-22 04:00 PM	
A1910	Install VB at SOG	2.0	08-Sep-22 04:00 PM	10-Sep-22 04:00 PM	
A1920	Install WWF at SOG	1.0	12-Sep-22 07:00 AM	12-Sep-22 06:00 PM	
A1930	Place & Finish SOG	2.0	13-Sep-22 07:00 AM	14-Sep-22 06:00 PM	
A2930	Saw cut Control Joints SOG	1.0	15-Sep-22 07:00 AM	15-Sep-22 06:00 PM	
A1940	Erect Steel Structure	8.0	16-Sep-22 07:00 AM	26-Sep-22 11:00 AM	-21.6
A1950	Plum and Brace Steel Structure	2.0	26-Sep-22 11:00 AM	28-Sep-22 11:00 AM	-21.6
A1960	Intstall Pan Decking Level 2	3.0	28-Sep-22 11:00 AM	01-Oct-22 12:00 PM	-21.6
A2910	Grout Column Baseplates	1.0	28-Sep-22 11:00 AM	29-Sep-22 11:00 AM	-6.6
A2920	Pour Back Dimonds	4.0	29-Sep-22 11:00 AM	04-Oct-22 02:00 PM	-6.6
A1970	Erect Stair 2	2.0	01-Oct-22 12:00 PM	04-Oct-22 02:00 PM	-21.6
A2940	Rough In Fire Protection	12.0	01-Oct-22 12:00 PM	15-Oct-22 04:00 PM	255.4
A1980	Install Pan Decking Roof	3.0	04-Oct-22 02:00 PM	07-Oct-22 02:00 PM	-21.6
A1990	Frame & Sheet Exterior Walls	12.0	07-Oct-22 02:00 PM	21-Oct-22 06:00 PM	-21.6
A2300	Install New RTU	8.0	07-Oct-22 02:00 PM	17-Oct-22 06:00 PM	28.4
A2960	Rough in MEP L2 Slab	4.0	07-Oct-22 02:00 PM	12-Oct-22 04:00 PM	82.4
A2970	Install WWF L2 Slab	4.0	12-Oct-22 04:00 PM	17-Oct-22 06:00 PM	82.4
A2950	Pour Elevated Slab L2	1.0	18-Oct-22 07:00 AM	18-Oct-22 06:00 PM	82.4
A2980	Pour Star 2 Stair Treads	4.0	19-Oct-22 07:00 AM	24-Oct-22 09:00 AM	82.4
A2000	Install Roofing on new Addition	12.0	22-Oct-22 08:00 AM	05-Nov-22 12:00 PM	24.4
A2010	Frame Interior Walls	25.0	22-Oct-22 08:00 AM	21-Nov-22 06:00 PM	-21.6
A2040	Install Curtainwalls and Store Fronts	30.0	22-Oct-22 08:00 AM	29-Nov-22 09:00 AM	-13.6
A2880	Temp cover as needed at W7 Line	4.0	29-Oct-22 10:00 AM	03-Nov-22 11:00 AM	240.4
A2030	Insulate and VB Exterior Walls	5.0	05-Nov-22 12:00 PM	11-Nov-22 02:00 PM	24.4
A2020	Rough In M.E.P.	30.0	22-Nov-22 07:00 AM*	29-Dec-22 04:00 PM	-21.6
A2800	Frame Hardlids and Soffits	8.0	22-Nov-22 07:00 AM	02-Dec-22 09:00 AM	8.4
A3110	Install Track for Folding Panel Partitio	2.0	22-Nov-22 07:00 AM	23-Nov-22 06:00 PM	221.4
A3140	Install Sunshades	15.0	29-Nov-22 09:00 AM	16-Dec-22 02:00 PM	-13.6
A2810	Install New Phase 2 windows	10.0	16-Dec-22 02:00 PM	29-Dec-22 04:00 PM	-13.6
A2050	Install Sound Insulation Interior Walls	8.0	29-Dec-22 04:00 PM	09-Jan-23 09:00 AM	-21.6

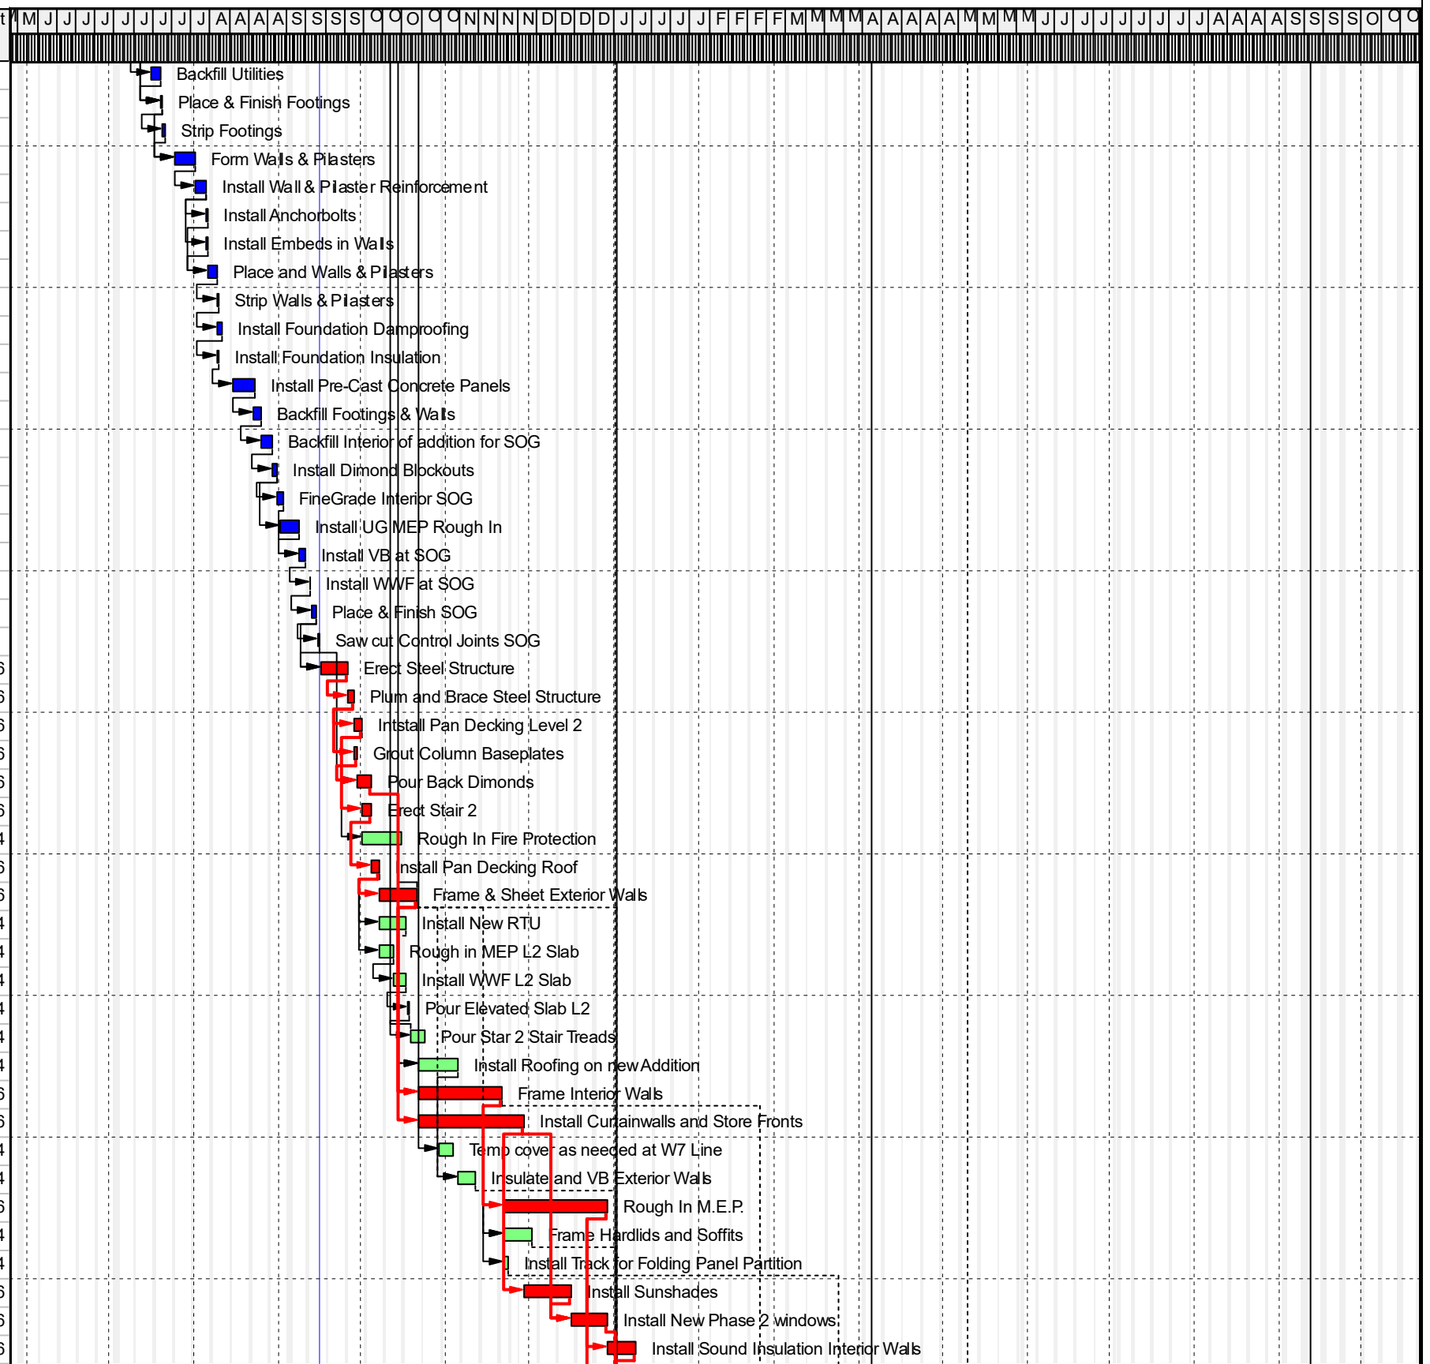

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
A2820	Start-up on New RTU	5.0	29-Dec-22 04:00 PM	04-Jan-23 06:00 PM	-18.6
A2060	Install GWB Interior	20.0	09-Jan-23 09:00 AM	01-Feb-23 04:00 PM	-21.6
A2070	Tape and Paint	20.0	01-Feb-23 04:00 PM	25-Feb-23 12:00 PM	-21.6
A2080	Install Ceiling Grid	12.0	25-Feb-23 12:00 PM	11-Mar-23 04:00 PM	-21.6
A2100	Install Ceiling Tiles	6.0	13-Mar-23 07:00 AM	20-Mar-23 09:00 AM	89.4
A2110	Install Door Frames	6.0	13-Mar-23 07:00 AM	20-Mar-23 09:00 AM	-21.6
A2130	Install Casework	6.0	13-Mar-23 07:00 AM	20-Mar-23 09:00 AM	89.4
A3000	Install Stainless Rails stair 2	4.0	13-Mar-23 07:00 AM	16-Mar-23 06:00 PM	-19.6
A2120	Install Flooring	10.0	20-Mar-23 09:00 AM	31-Mar-23 11:00 AM	89.4
A2310	Install Siding Phase 2	20.0	20-Mar-23 09:00 AM	12-Apr-23 04:00 PM	-21.6
A2140	Install Doors and Hardware	6.0	31-Mar-23 11:00 AM	07-Apr-23 02:00 PM	101.4
A2160	Trim M.E.P.	10.0	31-Mar-23 11:00 AM	12-Apr-23 04:00 PM	89.4
A3120	Install Folding Partition 153/155	2.0	31-Mar-23 11:00 AM	03-Apr-23 02:00 PM	117.4
A1650	Excavate for New Site Concrete	4.0	12-Apr-23 04:00 PM	17-Apr-23 06:00 PM	-21.6
A2150	Install Accessories	4.0	12-Apr-23 04:00 PM	17-Apr-23 06:00 PM	89.4
A2320	Install Rooftop Screen at RTU	6.0	12-Apr-23 04:00 PM	19-Apr-23 06:00 PM	-21.6
A2170	Install Furniture	4.0	18-Apr-23 07:00 AM	21-Apr-23 06:00 PM	89.4
A3010	Form, Place & Finish Site Concrete	20.0	18-Apr-23 07:00 AM	11-May-23 02:00 PM	-21.6
A2180	Contractor's Punchlist (Interior)	10.0	22-Apr-23 08:00 AM	04-May-23 11:00 AM	89.4
A3020	Intall SS Exterior Rails	4.0	11-May-23 02:00 PM	16-May-23 04:00 PM	80.4
A3030	Install Exterior Improvements	2.0	11-May-23 02:00 PM	13-May-23 02:00 PM	77.4
A3050	Install Paving & Striping	2.0	11-May-23 02:00 PM	13-May-23 02:00 PM	77.4
A3040	Install Exterior Landscaping	6.0	13-May-23 02:00 PM	20-May-23 04:00 PM	77.4
PCC II-3.9.3 PHASE 2 SUBSTANTIAL COMPLETION					
A2220	TAB Phase 2	4.0	12-Apr-23 04:00 PM	17-Apr-23 06:00 PM	100.4
A2830	Commissioning Phase 2	4.0	18-Apr-23 07:00 AM	21-Apr-23 06:00 PM	100.4
A2190	Final Cleaning	4.0	22-Apr-23 08:00 AM	27-Apr-23 09:00 AM	89.4
A2200	Owner's Punchlist	2.0	27-Apr-23 09:00 AM	29-Apr-23 10:00 AM	89.4
A2210	Punchlist Corrections	6.0	29-Apr-23 10:00 AM	06-May-23 12:00 PM	89.4
A2720	Obtain CCO for Phase 2	1.0	16-May-23 04:00 PM	17-May-23 04:00 PM	80.4
A2230	Substanital Completion Phase 2	0.0		17-May-23 04:00 PM	80.4
A2750	Start Warranty for Phase 2	0.0	17-May-23 04:00 PM		80.4
A3060	Owner Takes Possession Phase 2	0.0	17-May-23 04:00 PM		80.4
PCC II-3.4 PHASE 3					
PCC II-3.4.4 PHASE 3 PRE-DEMO					
A2240	Install Phase 3 Construction Barriers	7.0	09-Jan-23 02:00 PM	17-Jan-23 04:00 PM	34.0
A2250	Isolate Phase 3 Utillities	2.0	17-Jan-23 04:00 PM	19-Jan-23 04:00 PM	34.0
A2260	Install Neg Air and Scrubbers	2.0	17-Jan-23 04:00 PM	19-Jan-23 04:00 PM	34.0
A3160	User's Move out of Portion 2 (TH)	5.0	11-May-23 02:00 PM	17-May-23 04:00 PM	-21.6
A2420	Install Phase 3 Construction Barriers	4.0	11-May-23 02:00 PM	16-May-23 04:00 PM	-20.6
PCC II-3.4.1 PHASE 3 DEMO					
A2270	Demo Interior Finishes Portion 1	15.0	19-Jan-23 04:00 PM	07-Feb-23 11:00 AM	34.0
A2280	Install and Maintain FP systems	15.0	19-Jan-23 04:00 PM	07-Feb-23 11:00 AM	163.0
A2290	Demo Slab Trenches Phase 3	6.0	07-Feb-23 11:00 AM	14-Feb-23 02:00 PM	34.0
A2330	Demo or Abandon UG Pllumbing	4.0	14-Feb-23 02:00 PM	18-Feb-23 02:00 PM	34.0
A3150	Demo Interior Finishes Portion 2 (TH	6.0	17-May-23 04:00 PM	24-May-23 06:00 PM	-21.6

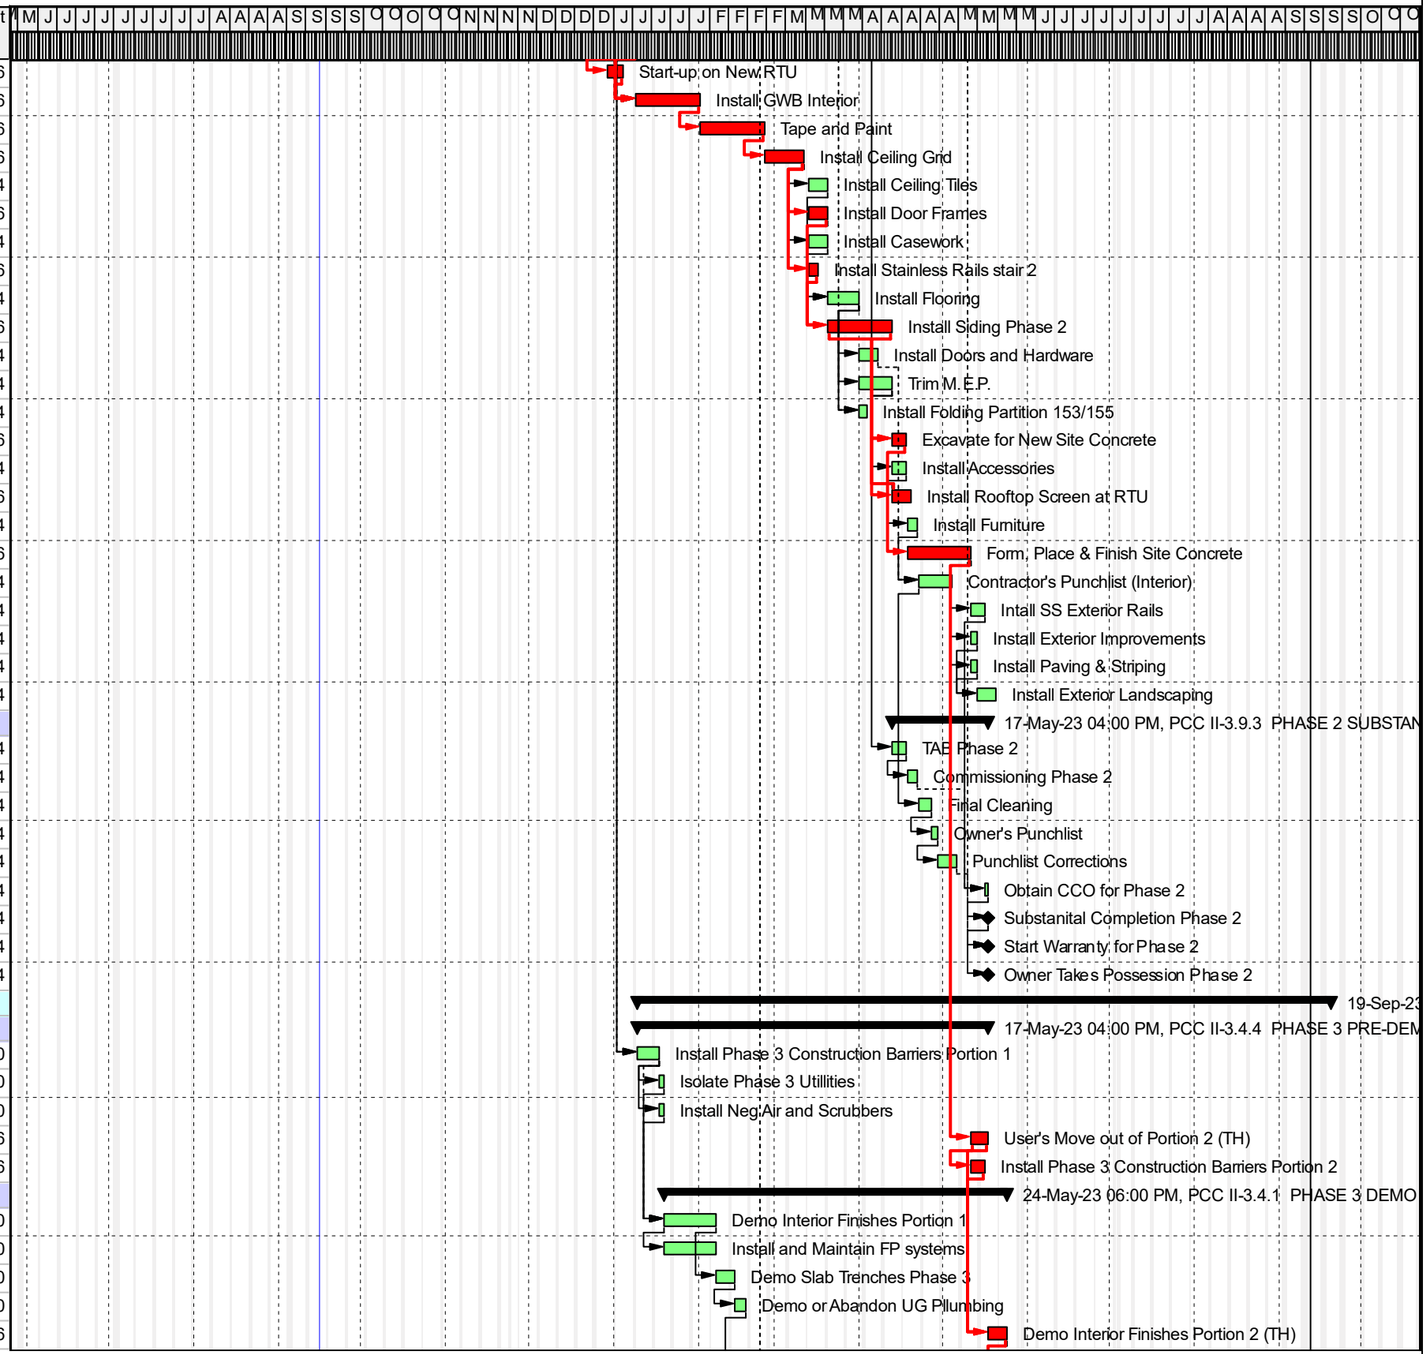

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
PCC II-3.4.2 PHASE 3 BUILDOUT PORTION 1					
A2840	Rough In UG Plumbing	6.0	18-Feb-23 02:00 PM	25-Feb-23 04:00 PM	34.0
A2340	Pour Back Trench Cut-outs	2.0	27-Feb-23 07:00 AM	28-Feb-23 06:00 PM	34.0
A2350	Pour Recessed Slab for Sound Boot	2.0	01-Mar-23 07:00 AM	02-Mar-23 06:00 PM	34.0
A2360	Frame Walls	20.0	03-Mar-23 07:00 AM	27-Mar-23 04:00 PM	34.0
A3070	Rough In New FP System	12.0	03-Mar-23 07:00 AM	17-Mar-23 11:00 AM	89.0
A2370	Frame Soffits and Hardlids	20.0	21-Mar-23 02:00 PM	14-Apr-23 09:00 AM	106.0
A2380	Rough In M.E.P.	25.0	21-Mar-23 02:00 PM	20-Apr-23 11:00 AM	34.0
A2390	Install Sound Insulation	8.0	27-Mar-23 04:00 PM	05-Apr-23 06:00 PM	37.0
A2400	Install GWB	20.0	06-Apr-23 07:00 AM	29-Apr-23 02:00 PM	37.0
A3130	Install Track for Sliding Glass Partitior	2.0	14-Apr-23 09:00 AM	17-Apr-23 11:00 AM	106.0
A2410	Tape and Paint	20.0	18-Apr-23 11:00 AM	11-May-23 06:00 PM	37.0
A2610	Remove and Replace RTU 1	5.0	20-Apr-23 11:00 AM	26-Apr-23 02:00 PM	34.0
A2620	Tie In new RTU to system	10.0	26-Apr-23 02:00 PM	08-May-23 06:00 PM	34.0
A2560	Trim M. E.P.	12.0	09-May-23 07:00 AM	23-May-23 11:00 AM	34.0
A2440	Install Demountable Partitions	8.0	12-May-23 07:00 AM	22-May-23 11:00 AM	59.0
A2450	Install Specialty Doors (side folding)	7.0	12-May-23 07:00 AM	20-May-23 10:00 AM	60.0
A2510	Install Casework	8.0	12-May-23 07:00 AM	22-May-23 11:00 AM	59.0
A2520	Install Door Frames	6.0	12-May-23 07:00 AM	19-May-23 09:00 AM	37.0
A3080	Install Displays	4.0	12-May-23 07:00 AM	17-May-23 09:00 AM	39.0
A2470	Install Ceiling Grid	16.0	19-May-23 09:00 AM	08-Jun-23 04:00 PM	37.0
A2550	Install finishes & accessories	6.0	23-May-23 11:00 AM	31-May-23 02:00 PM	34.0
A2530	Install Doors and Hardware	8.0	31-May-23 02:00 PM	09-Jun-23 04:00 PM	34.0
A2490	Install Ceiling Tiles	8.0	08-Jun-23 04:00 PM	19-Jun-23 09:00 AM	37.0
A2500	Install Flooring	12.0	19-Jun-23 09:00 AM	03-Jul-23 02:00 PM	37.0
A2540	Install HD-2 Shelving Unit Complete	4.0	29-Jun-23 11:00 AM	05-Jul-23 02:00 PM	37.0
A2580	Install Furniture & Equipment	6.0	03-Jul-23 02:00 PM	11-Jul-23 04:00 PM	37.0
PCC II-3.4.5 PHASE 3 BUILDOUT PORTION 2					
A3180	Frame Walls	15.0	25-May-23 07:00 AM	13-Jun-23 02:00 PM	-21.6
A3240	Install new Exterior Windows	13.0	25-May-23 07:00 AM	10-Jun-23 12:00 PM	6.4
A3190	Frame Soffits and Hardlids	10.0	13-Jun-23 02:00 PM	24-Jun-23 04:00 PM	-5.6
A3200	Rough In M.E.P.	20.0	13-Jun-23 02:00 PM	08-Jul-23 10:00 AM	-15.6
A3220	Install Sound Insulation	6.0	13-Jun-23 02:00 PM	20-Jun-23 04:00 PM	-21.6
A3290	Install Interior Storefronts	6.0	13-Jun-23 02:00 PM	20-Jun-23 04:00 PM	-1.6
A3210	Rough In New FP System	6.0	13-Jun-23 02:00 PM	20-Jun-23 04:00 PM	13.4
A3250	Install Track for Sliding Glass Partitior	2.0	13-Jun-23 02:00 PM	15-Jun-23 02:00 PM	-17.6
A3230	Install GWB	20.0	20-Jun-23 04:00 PM	15-Jul-23 12:00 PM	-21.6
A3270	Tape and Paint	15.0	15-Jul-23 12:00 PM	02-Aug-23 06:00 PM	-21.6
A3320	Install Sliding Glass Partition Wall	4.0	15-Jul-23 12:00 PM	20-Jul-23 02:00 PM	-2.6
A3350	Install Restroom Tile	6.0	15-Jul-23 12:00 PM	22-Jul-23 02:00 PM	4.4
A3390	Install finishes & accessories	6.0	22-Jul-23 02:00 PM	29-Jul-23 04:00 PM	4.4
A3380	Trim M. E.P.	12.0	22-Jul-23 02:00 PM	07-Aug-23 09:00 AM	4.4
A3300	Install Demountable Partitions	2.0	03-Aug-23 07:00 AM	04-Aug-23 06:00 PM	-15.6
A3370	Install Ceiling Grid	8.0	03-Aug-23 07:00 AM	12-Aug-23 10:00 AM	-21.6
A3340	Install Door Frames	4.0	03-Aug-23 07:00 AM	08-Aug-23 09:00 AM	-17.6
A3410	Install Doors and Hardware	4.0	08-Aug-23 09:00 AM	12-Aug-23 10:00 AM	-17.6

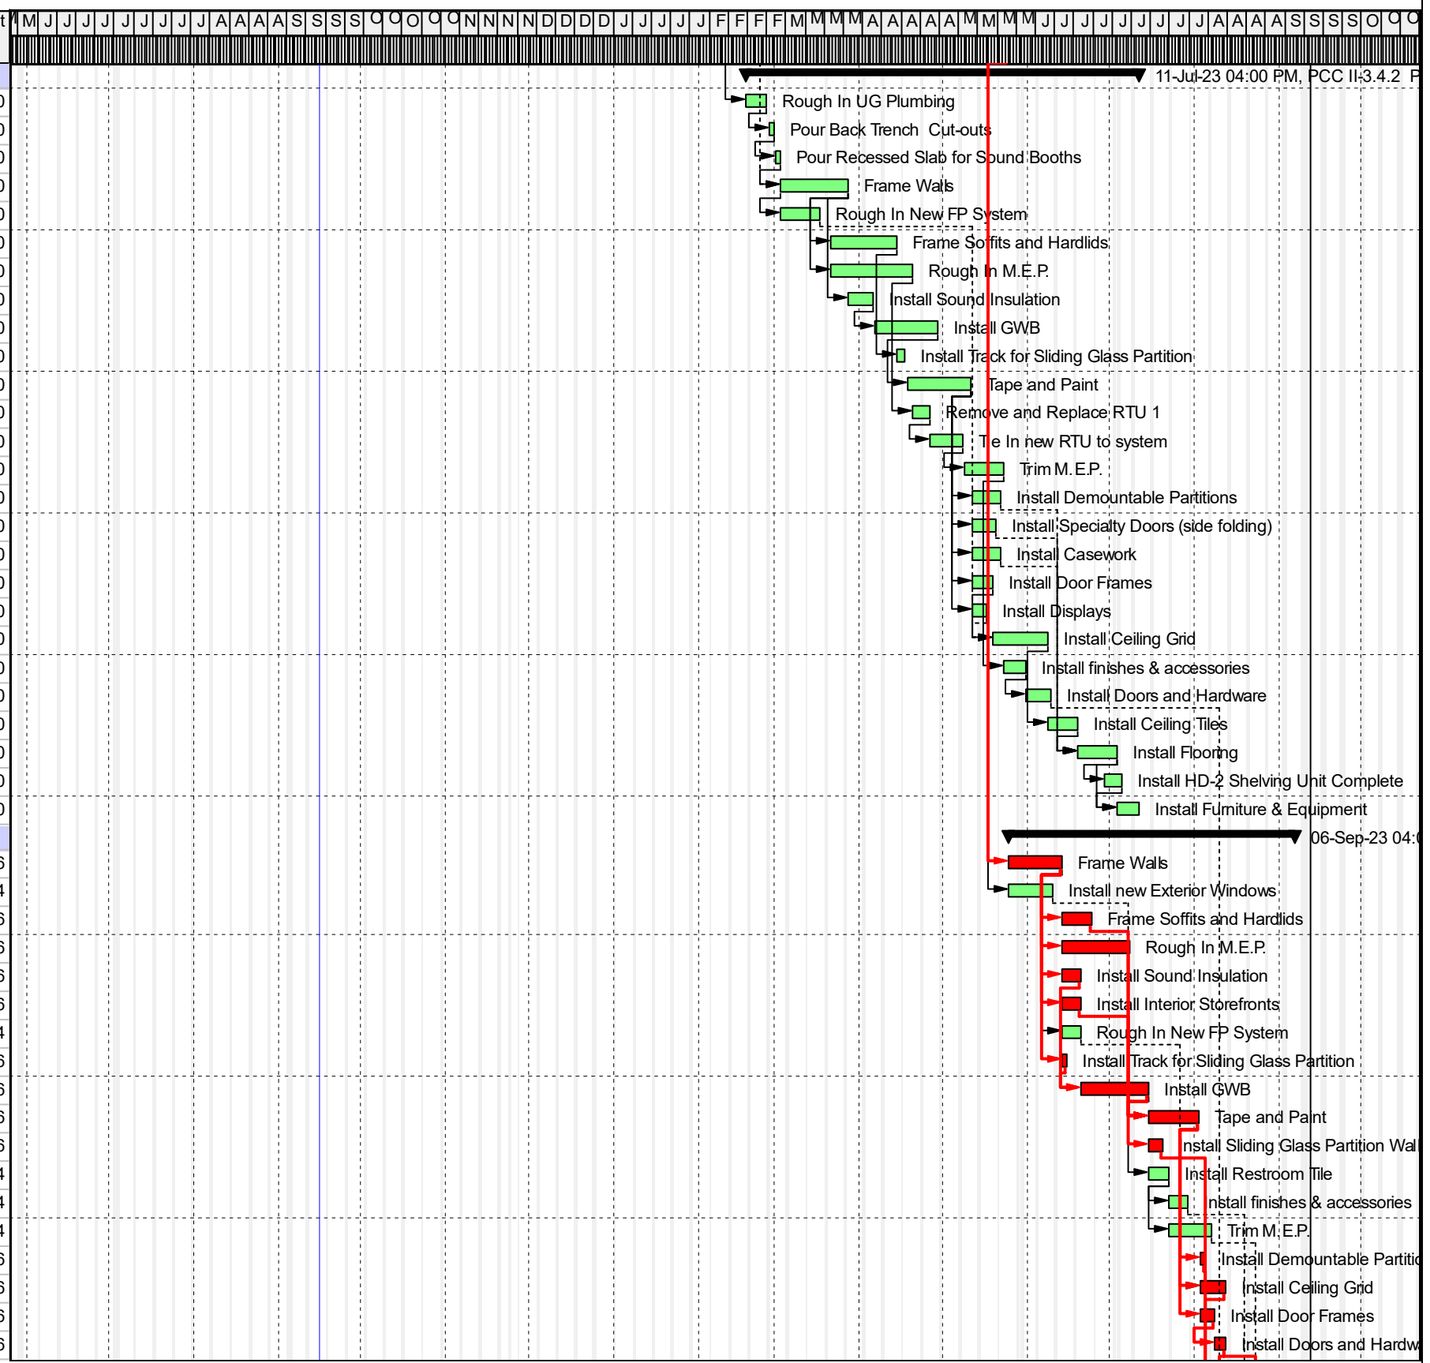

Remaining Level of Effort | Actual Work | Critical Remaining Work
Actual Level of Effort | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
A3420	Install Ceiling Tiles	4.0	12-Aug-23 10:00 AM	17-Aug-23 11:00 AM	-21.6
A3430	Install Flooring	10.0	17-Aug-23 11:00 AM	29-Aug-23 04:00 PM	-14.6
A3330	Install Casework	8.0	17-Aug-23 11:00 AM	26-Aug-23 02:00 PM	-18.6
A3440	Install Furniture & Equipment	3.0	26-Aug-23 02:00 PM	30-Aug-23 04:00 PM	-18.6
A3450	Contractor's Punchlist	5.0	30-Aug-23 04:00 PM	06-Sep-23 04:00 PM	-15.6
PCC II-3.4.3	PHASE 3 SUBSTANTIAL COMPLETION				
A2640	TAB Phase 3	4.0	17-Aug-23 11:00 AM	22-Aug-23 02:00 PM	-21.6
A2650	Commissioning Phase 3	4.0	22-Aug-23 02:00 PM	26-Aug-23 02:00 PM	-21.6
A2700	Obtain CCO for Phase 3	4.0	26-Aug-23 02:00 PM	31-Aug-23 04:00 PM	-11.6
A2590	Final Cleaning	4.0	30-Aug-23 04:00 PM	05-Sep-23 04:00 PM	-18.6
A2850	Substanital Completion Phase 3	0.0		31-Aug-23 04:00 PM	-11.6
A2600	Owner's Punchlist	4.0	05-Sep-23 04:00 PM	11-Sep-23 04:00 PM	-18.6
A2630	Punchlist Corrections	6.0	11-Sep-23 04:00 PM	19-Sep-23 04:00 PM	-18.6
A2740	Start Warranty for Phase 3	0.0	19-Sep-23 04:00 PM		-18.6
A3090	Owner Takes Possession	0.0		19-Sep-23 04:00 PM	-18.6
PCC II-3.7	PROJECT CLOSEOUT				
A2670	Owner Training	4.0	22-Aug-23 02:00 PM	26-Aug-23 02:00 PM	-1.6
A2680	Submit O&M's	20.0	26-Aug-23 02:00 PM	22-Sep-23 04:00 PM	-21.6
A2690	Submit Reoprts and other Close-out	20.0	26-Aug-23 02:00 PM	22-Sep-23 04:00 PM	-21.6
A2660	Demobilize	6.0	31-Aug-23 04:00 PM	08-Sep-23 04:00 PM	-11.6
PCC II-3.8	PROJECT COMPLETION				
A2710	Obtain Ful C.O.	1.0	31-Aug-23 04:00 PM	01-Sep-23 04:00 PM	-6.6
A2730	Project Complete	0.0		19-Sep-23 04:00 PM*	-18.6

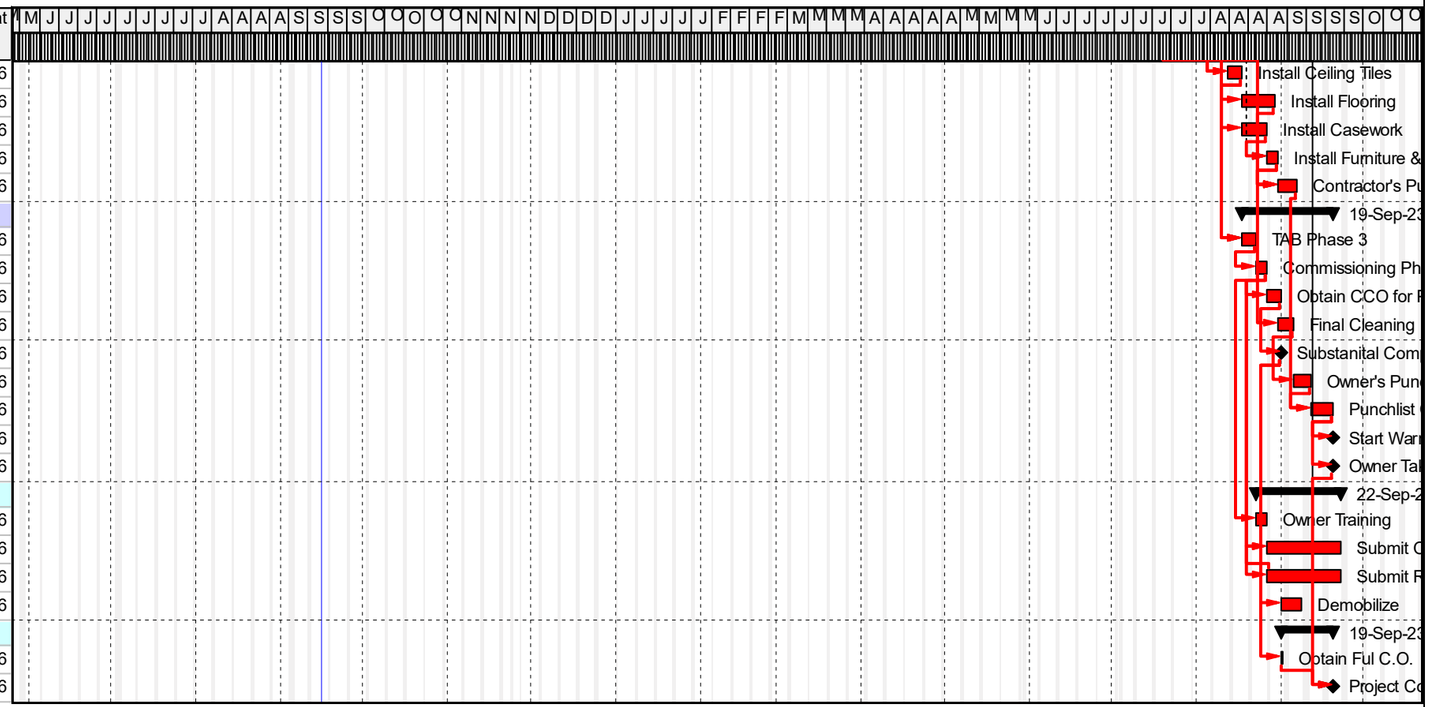

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

TASK filter: All Activities

© Oracle Corporation
